


JMPS Product IPT




7/28/98

Joint Mission Planning

DATE: 28 July 1998

PRESENTER: Paul Bielewicz

Outline




7/28/98

Joint Mission Planning

- Status
- Issues
- FY99 Plans
- TAMPS Master Product IPT

Notional Acquisition Schedule



7/28/98


Joint Mission Planning

Formal RFP	23 May 98	
Proposals Due	2 July 98	
Source Selection	7 July 98	
Team leader training	29 June 98	
Team training	7 July 98	
Evaluations Complete	26 August 98	
SSEB Convenes	27 August 98	
SSAC Brief	1 September 98	
SSA Brief	1 September 98	
Phase I Contract Award	4 September 98	
Phase I Contract Award (w/disc)	29 October 98	
Phase II Contract Award		
earliest planned	11 March 99	
latest planned	28 June 99	

Complete

In work

FY-98 Tasks



7/28/98

Joint Mission Planning

Acquisition Documentation RFP Package

(AP/APB/SAMP/TEMP)

Lead - Paul Bielewicz

Temp Lead - LT D'Acquisti

Lead - Wallace Coggi

Support - all

CONOPS

(IMPWG, Users Conferences)

Lead - Kerry Neace

Support - Linda Waymire

Marc Espitia

Source Selection

Lead - Wallace Coggi

Support - all

Cost Analysis

Lead - Air 4.2

Micheline Lopez-Estrada

Requirements Database

(PRISM/DOORS)

Lead - Ruth Swick

Support - Draper Team,

Logistics

Lead - Paul Steinbacher

Technical

Documentation

(SSG/SOO)

Lead - Kerry Wilson


Home Page / Virtual Office

TBD

Change

No Change

FY-98 Tasks Update



7/28/98

Joint Mission Planning

Acquisition Documentation

(AP/APB/SAMP/TEMP)

Lead - Paul Bielewicz

Temp Lead - LT

CONOPS

(Acquisition)

(IMPWG, Users Conferences)

Lead - Kerry Neace

Support - Linda Waymire

Marc Espitia

Requirements Database

(PRISM/DOORS)

Lead - Ruth Swick

Support - Draper Team,

BAI

Logistics

Lead - Paul Steinbacher

- AP has been signed
- APB in work
- SAMP/TEMP in work
- C4I Support Plan (JSF)

CONOPS

- Balance of MPMs to be contacted (to date 17 of 28)

- Joint requirements process in work

- PRISM


- Report in on 17 MPMs

- Preparing Brief for

Change

No Change

FY-98 Tasks



7/28/98

Joint Mission Planning

- RFP released 23 May
- Industry responses due 2 July

RFP Package

Lead - Wallace Coggin

Support - all

- Source Selection 7/7 - 8/28

Source Selection

Lead - Wallace Coggin

Support - all

- Electronic Room
(Training - 7 Jul)
- SSAC for Phases I and II

- ICE updated for Phase I&II
- LCC prior to Phase I award

Cost Analysis

Lead - Air 4.2

Micheline Lopez-Est

- Working on SSS

Technical

Documentation

(SSG/SOO)

Lead - Kerry Wilson


- Home Page
 - Verifying access list
 - slow progress w/ VO

Home Page / Virtual

Office

TBD

JMPS Issues



7/28/98

Joint Mission Planning

- **Issue:** Joint Requirements Validation & Prioritization

Recommendation: JMPS IPT is working on defining the process.


Resolution: Process to be briefed at next JPEB

- **Issue:** Mr. Gilligan, PEO(BA) expressed concern about how will contractors keep team together during down select period (unfunded)

Recommendation: Discuss with contracts and contractors on how much funding would be required and include these in cost estimates.

Resolution: None

JMPS Issues (cont.)



7/28/98

Joint Mission Planning

- **Issue:** JMPS is planning on developing a Test Suite component. The component will be common, expense will be shared with with the Air Force. Discussing at the JMPS IPT level to determine if it is Government or Contractor developed and compiling a list of possible providers.

Recommendation: Need thoughts and recommendation of the Leadership team


Resolution: None

- **Issue:** JMPS requires a compatibility lab for software integration and testing. Discussing at the JMPS IPT level to determine if it is joint or service independent and Government or Contractor facility.

Recommendation: Need thoughts and recommendation of the Leadership team

Resolution: None

JMPS Issues (cont.)



7/28/98


Joint Mission Planning

- **Issue:** What is the JMPS IPT to deliver to the PMAs for their 50K contribution and are these funds included in the JMPS budget (ie. will our budget be increased by these funds or stay the same?)

Recommendation: Have Requirements and BFM determine the process and brief at the next IPT Status Brief

Resolution: None

FY 99 Tasks



7/28/98

Joint Mission Planning

System Engineering

NAWC

DRC

BAI

Requirements

NAWC

CSCI

BAI

Draper

Test Suite Development

TBD

Acquisition Support

Delfin

Cost Support

NAWC

AIR4.2

Logistics Support

SPAWAR

PFPS Rearchitecture

46th Squadron

Compatibility Lab


TBD

Contract

TBD


Other - PMA travel and NAWC travel and ODC

Risk Analysis and Risk Mitigation




7/28/98

Joint Mission Planning

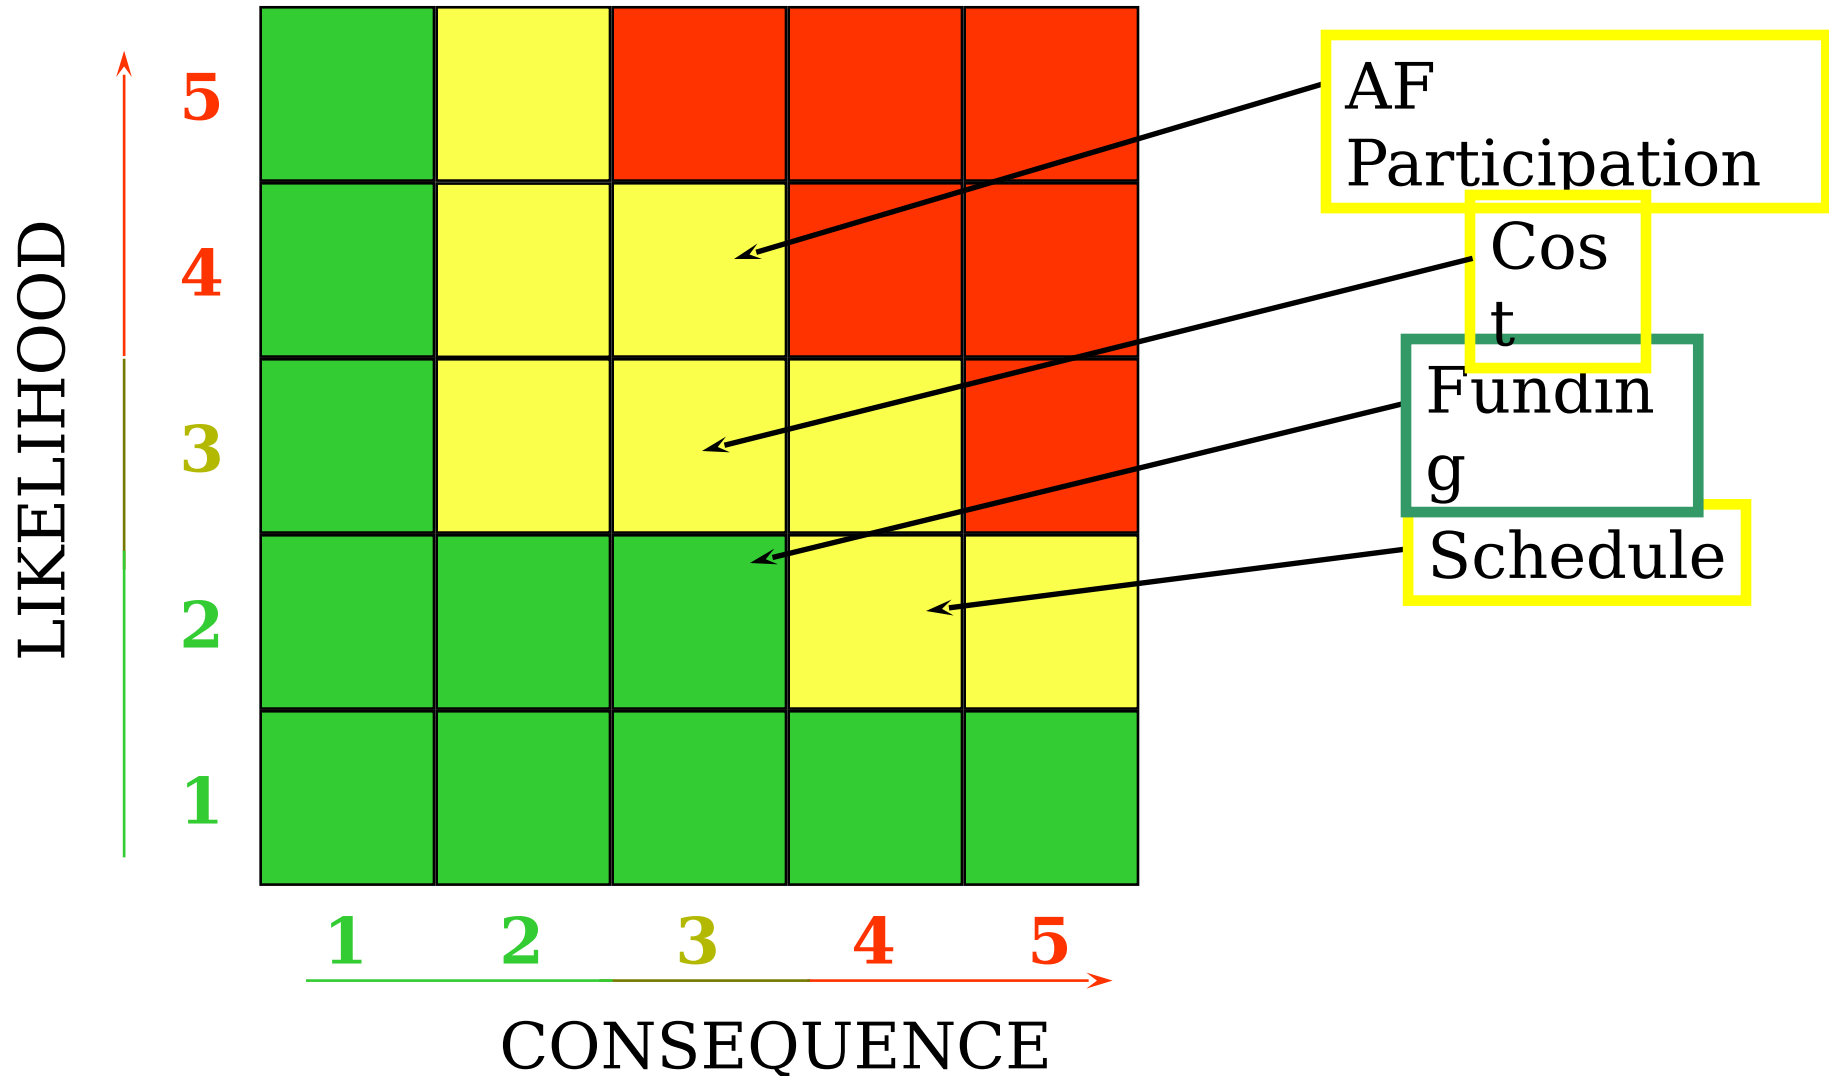

JMPS

Mitigation




7/28/98

Joint Mission Planning

- **Schedule**
 - Track ATR
 - Streamline Formal Source Selection
- **Funding**
- **Air Force Participation**
 - LCOL Thorn briefing MAJCOMs - solidifying support
- **Cost**
 - Cost estimate based on old data (updated with offerors estimate)
 - Need LCC for Phase I contract award (in work, AIR-4.2)


Overall Status




7/28/98

Joint Mission Planning

Funding




or




without
Air
Force


Cost




Schedule




Performance



Global



JMPS Master Product IPT



7/28/98

Joint Mission Planning

TAMPS/JMPS Product IPT													Assessment Indicator											
PROGRAM STAFF		ACAT	IV (T)		Participating Serv.		Units		Program Cost															
Phase		Pre EMD																						
Next MS Event		MS II																						
MS Date		Nov-98																						
MS Status		N/A		Contractors		Unit Cost																		
AS OF													1998											
28-Dec-97													APPROVED											
Task Name													1997		1998									
1. Plan/Implement/Close													Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
2. Plan													PEB 9/12											
3. COG OPS																								
4. Task/OPF																								
5. Software Integ. Maturity Matrix																								
6. Program Review																								
7. PEB																								
8. Contract Award																								
9. Milestone II																								

TAMPS JMPS Product IPT

Assessment Indicator

Yellow

PROGRAM STAFF	ACAT	IV (T)	Participating Serv.	Units	Program Cost
PM: CAPT. Spilman	Phase	Pre EMD	USN	Dev:	(\$M TY \$)
DPM: Ms. O. Stinson	Next MS Event	MS II	USAF	Fleet:	R&D: 51.5
IPT Lead Level 1:	MS Date	Apr-99		Ordered:	Proc: 15.6
LCOL Thom	MS Status	N/A	Contractors	Unit Cost	Other: 16.8
AS OF	APPROVED				O&MN: 12M Shtfall
28-Jul-98	CAPT T. L. Spilman				Total: 83.9

FY00: 6.7 8.0 6.8 9.2 9.4 8.5 482 CSS Office
 OFN 1.2 1.7 1.9 1.9 0.0 6.7 NAMCND
 O&MN 0.0 SSS-Office
 QTY 6.7 8.6 8.0 10.9 11.3 10.4 55.9 Training Te
 Mgt Reserve
 Data: FY 98 FY 99 FY 00 FY 01 FY 02 FY 03 TOTAL AR 4.2
 RDTSE 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 OFN 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 O&MN 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 QTY 5.4 5.4 5.4 5.4 5.4 5.4 5.4
 RDTSE 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 OFN 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 O&MN 0.0 0.0 0.0 0.0 0.0 0.0 0.0
 QTY 0.0 0.0 0.0 0.0 0.0 0.0 0.0


IPT Comments & Issues:
 Cost: Increased by \$48M without AF
 Schedule: June Aw and Target Fleet release 01
 Funding: Need to relocate \$10M from FY 00 (3) to FY 01 to FY 00 (1). O&MN Funding was not identified for this effort
 Shortfall of \$20M. Management Reserve of \$450k for
 Name conversion. Source Selection and COMOPS task and
 Source Selection Support. FY 99 and FY 00 funding less than
 expected to cover framework on contract (23.5M available)
 Contract Status: June Aw and Target. Tech Lead for Source
 Selection
 Mgt & Global Issues: J REB direction
 Documentation Status: Need Logistics Support

Joint Mission Planning

[illegible]

Under FY 98 FY 99 FY 00 FY 01 FY 02 FY 03 TOTAL												New BERGE Doc BERGE COPS/SP CQ/N TOTAL												2004																																			
Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2 Q3 Q4 Q1 Q2																																																											
Contract Q3 6.7 8.6 6.8 9.2 9.4 8.5 48.2 C55 C100 C/N 1.2 1.7 1.9 1.9 6.7 NAWMO 0.0 SES Office Q3 6.7 8.6 8.0 10.9 11.3 10.4 55.9 Class EX 98 FY 99 FY 00 FY 01 FY 02 FY 03 TOTAL A/R 4.2 RCSA 0.9 0.9 APL OPN 0.0 TSCM CQ/N 0.0 PFPS QTY 0.0 Taxes Total 5.4 RCSA 5.4 OPN 0.0 CQ/N 0.0 QTY 0.0 Total 5.4 Execution												1 Contract												98																																			
FY Comments: Issues: Cost: Increased by \$48M w/out AF Schedule: June Rev and Target/Rev release 01 Funding: Need to relocate \$10M from FY 02/03 (\$M4M) to FY 00/01. OMAA funding was not identified for this effort. Shortfall of \$20M. Management Reserve of \$450k is for Henscom rotation, Source Selection and CONOPS travel and Source Selection Support. FY 99 and FY 00 funding less than expected to cover Framework contract (23.9M available). Contract Status: June Forward Target. Tech Lead for Source Selection. Mngt & Global Issues: JPEB direction. Documentation Status: Need Logistics Support.												4 IOCs												1999																																			
Assessment Technical Cost Schedule Software Funding Test & E Productive Logistics Contract Mngt & C Documents												8 Migration Study												2000																																			
9 Framework												2001												2002												2003												2004											
10 Flt Png Capability												2001												2002												2003												2004											
11 Combat Png Capability												2001												2002												2003												2004											
12 Strike/Force Png Capability												2001												2002												2003												2004											
13 Milestone/JPEB												2001												2002												2003												2004											
14 All Hands												2001												2002												2003												2004											

JMPS Master Product IPT




7/28/98

Joint Mission Planning

TAMPS JMPS Product IPT																	Assessment Indicator																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
PROGRAM STAFF		ACAT	W/T		Participating Serv.		Units		Program Cost																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Phase		PWS EMD																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
Next MS Event		MS II																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
MS Date		Nov-98																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
MS Status		N/A								Contractors		Unit Cost																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
AS OF 18-Dec-97																	APPROVED																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
18-Dec-97																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
1997																	1998																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Task Name																	Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan		Jan</	


JMPS Master Product IPT



7/28/98

Joint Mission Planning

TAMPS/JMPS Product IPT													Assessment Indicator												
PROGRAM STAFF		ACAT	RV (F)		Participating Serv.		Units		Program Cost																
		Phase	Pre-EMD																						
		Next MS Event	MSB																						
		MS Date	Nov98																						
		MS Status	N/A		Contractors		Unit Cost																		
AS OF 30-Dec-97 APPROVED																									
ID	Task Name	1997												1998											
		Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
1	101 Release/Close																								
2	102																								
3	103																								
4	104																								
5	105																								
6	106																								
7	107																								
8	108																								
9	109																								
PER MS 11-12																									
1	101																								
2	102																								
3	103																								
4	104																								
5	105																								
6	106																								
7	107																								
8	108																								
9	109																								
10	110																								
11	111																								
12	112																								
13	113																								
14	114																								
15	115																								
16	116																								
17	117																								
18	118																								
19	119																								
20	120																								
21	121																								
22	122																								
23	123																								
24	124																								
25	125																								
26	126																								
27	127																								
28	128																								
29	129																								
30	130																								
31	131																								
32	132																								
33	133																								
34	134																								
35	135																								
36	136																								
37	137																								
38	138																								
39	139																								
40	140																								
41	141																								
42	142																								
43	143																								
44	144																								
45	145																								
46	146																								
47	147																								
48	148																								
49	149																								
50	150																								
51	151																								
52	152																								
53	153																								
54	154																								
55	155																								
56	156																								
57	157																								
58	158																								
59	159																								
60	160																								
61	161																								
62	162																								
63	163																								
64	164																								
65	165																								
66	166																								
67	167																								
68	168																								
69	169																								
70	170																								
71	171																								
72	172																								
73	173																								
74	174																								
75	175																								
76	176																								
77	177																								
78	178																								
79	179																								
80	180																								
81	181																								
82	182																								
83	183																								
84	184																								
85	185																								
86	186																								
87	187																								
88	188																								
89	189																								
90	190																								
91	191																								
92	192																								
93	193																								
94	194																								
95	195																								
96	196																								
97	197																								
98	198																								
99	199																								
100	200																								
101	201																								
102	202																								
103	203																								
104	204																								
105	205																								
106	206																								
107	207																								
108	208																								
109	209																								
110	210																								
111	211																								
112	212																								
113	213																								
114	214																								
115	215																								
116	216																								
117	217																								
118	218																								
119	219																								
120	220																								
121	221																								
122	222																								
123	223																								
124	224																								
125	225																								
126	226																								
127	227																								
128	228																								
129	229																								
130	230																								
131	231																								
132	232																								
133	233																								
134	234																								
135	235																								
136	236																								
137	237																								
138	238																								
139	239																								
140	240																								
141	241																								
142	242																								
143	243																								
144	244																								
145	245																								
146	246																								
147	247																								
148	248																								
149	249																								
150	250																								
151	251																								
152	252																								
153	253																								
154	254																								
155	255																								
156	256																								
157	257																								
158	258																								
159	259																								
160	260																								
161	261																								
162	262																								
163	263																								
164	264																								
165	265																								
166	266																								
167	267																								
168	268																								
169	269																								
170	270																								
171	271																								
172	272																								
173	273																								
174	274																								
175	275																								
176	276																								
177	277																								
178	278																								
179	279																								
180	280																								
181	281																								
182	282																								
183	283																								
184	284																								
185	285																								
186	286																								
187	287																								
188	288																								
189	289																								
190	290																								
191	291																								
192	292																								
193	293																								
194	294																								
195	295																								
196	296																								
197	297																								
198	298																								
199	299																								
200	300																								
201	301																								
202	302																								
203	303																								
204	304																								
205	305																								
206	306																								
207	307																								
208	308																								
209	309																								
210	310																								
211	311																								
212	312																								
213	313																								
214	314																								
215	315																								
216	316																								
217	317																								
218	318																								
219	319																								
220	320																								
221	321																								
222	322																								
223	323																								
224	324																								
225	325																								
226	326																								
227	327																								
228	328																								
229	329																								
230	330																								
231	331																								
232	332																								
233	333																								
234	334																								
235	335																								
236	336																								
237	337																								
238	338																								
239	339																								
240	340																								
241	341																								
242	342																								
243	343																								
244	344																								
245	345																								
246	346																								
247	347																								
248	348																								
249	349																								
250	350																								
251	351																								
252	352																								
253	353																								
254	354																								
255	355																								
256	356																								
257	357																								
258	358																								
259	359																								
260	360																								
261	361																								
262	362																								
263	363																								
264	364																								
265	365																								
266	366																								
267	367																								
268	368																								
269	369																								
270	370																								
271	371																								
272	372																								
273	373																								
274	374																								
275	375																								
276	376																								
277	377																								
278	378																								
279	379																								
280	380																								
281	381																								
282	382																								
283	383																								
284	384																								
285	385																								
286	386																								
287	387																								
288	388																								
289	389																								
290	390																								
291	391																								
292	392																								
293	393																								
294	394																								
295	395																								
296	396																								
297	397																								
298	398																								
299	399																								
300	400																								
301	401																								
302	402																								
303	403																								
304	404																								
305	405																								
306	406																								
307	407																								
308	408																								
309	409																								
310	410																								
311	411																								
312	412																								
313	413																								
314	414																								
315	415																								
316	416																								
317	417																								
318	418																								
319	419																								
320	420																								
321	421																								
322	422																								
323	423																								
324	424																								
325	425																								
326	426																								
327	427																								
328	428																								
329	429																								
330	430																								
331	431																								
332	432																								
333	433																								
334	434																								
335	435																								
336	436																								
337	437																								
338	438																								
339	439																								
340	440																								
341	441																								
342	442																								
343	443																								
344	444																								
345	445																								
346	446																								
347	447																								
348	448																								
349	449																								
350	450																								
351	451																								
352	452																								
353	453																								
354	454																								
355	455																								
356	456																								
357	457																								
358	458																								
359	459																								
360	460																								
361	461																								
362	462																								
363	463																								
364	464																								
365	465																								
366	466																								
367	467																								
368	468																								
369	469																								
370	470																								
371	471																								
372	472																								
373	473																								
374	474																								
375	475																								
376	476																								
377	477																								
378	478																								
379	479																								
380	480																								
381	481																								
382	482																								
383	483																								
384	484																								
385	485																								
386	486																								
387	487																								
388	488																								
389	489																								
390	490																								
391	491																								
392	492																								
393	493																								
394	494																								
395	495																								
396	496																								
397	497																								
398	498																								
399	499																								
400	500																								
401	501																								
402	502																								
403	503																								
404	504																								
405	505																								
406	506																								
407	507																								
408	508																								
409	509																								
410	510																								
411	511																								
412	512																								
413	513																								
414	514																								
415	515																								
416	516																								
417	517																								
418	518																								



7/28/98

Joint Mission Planning

Questions
